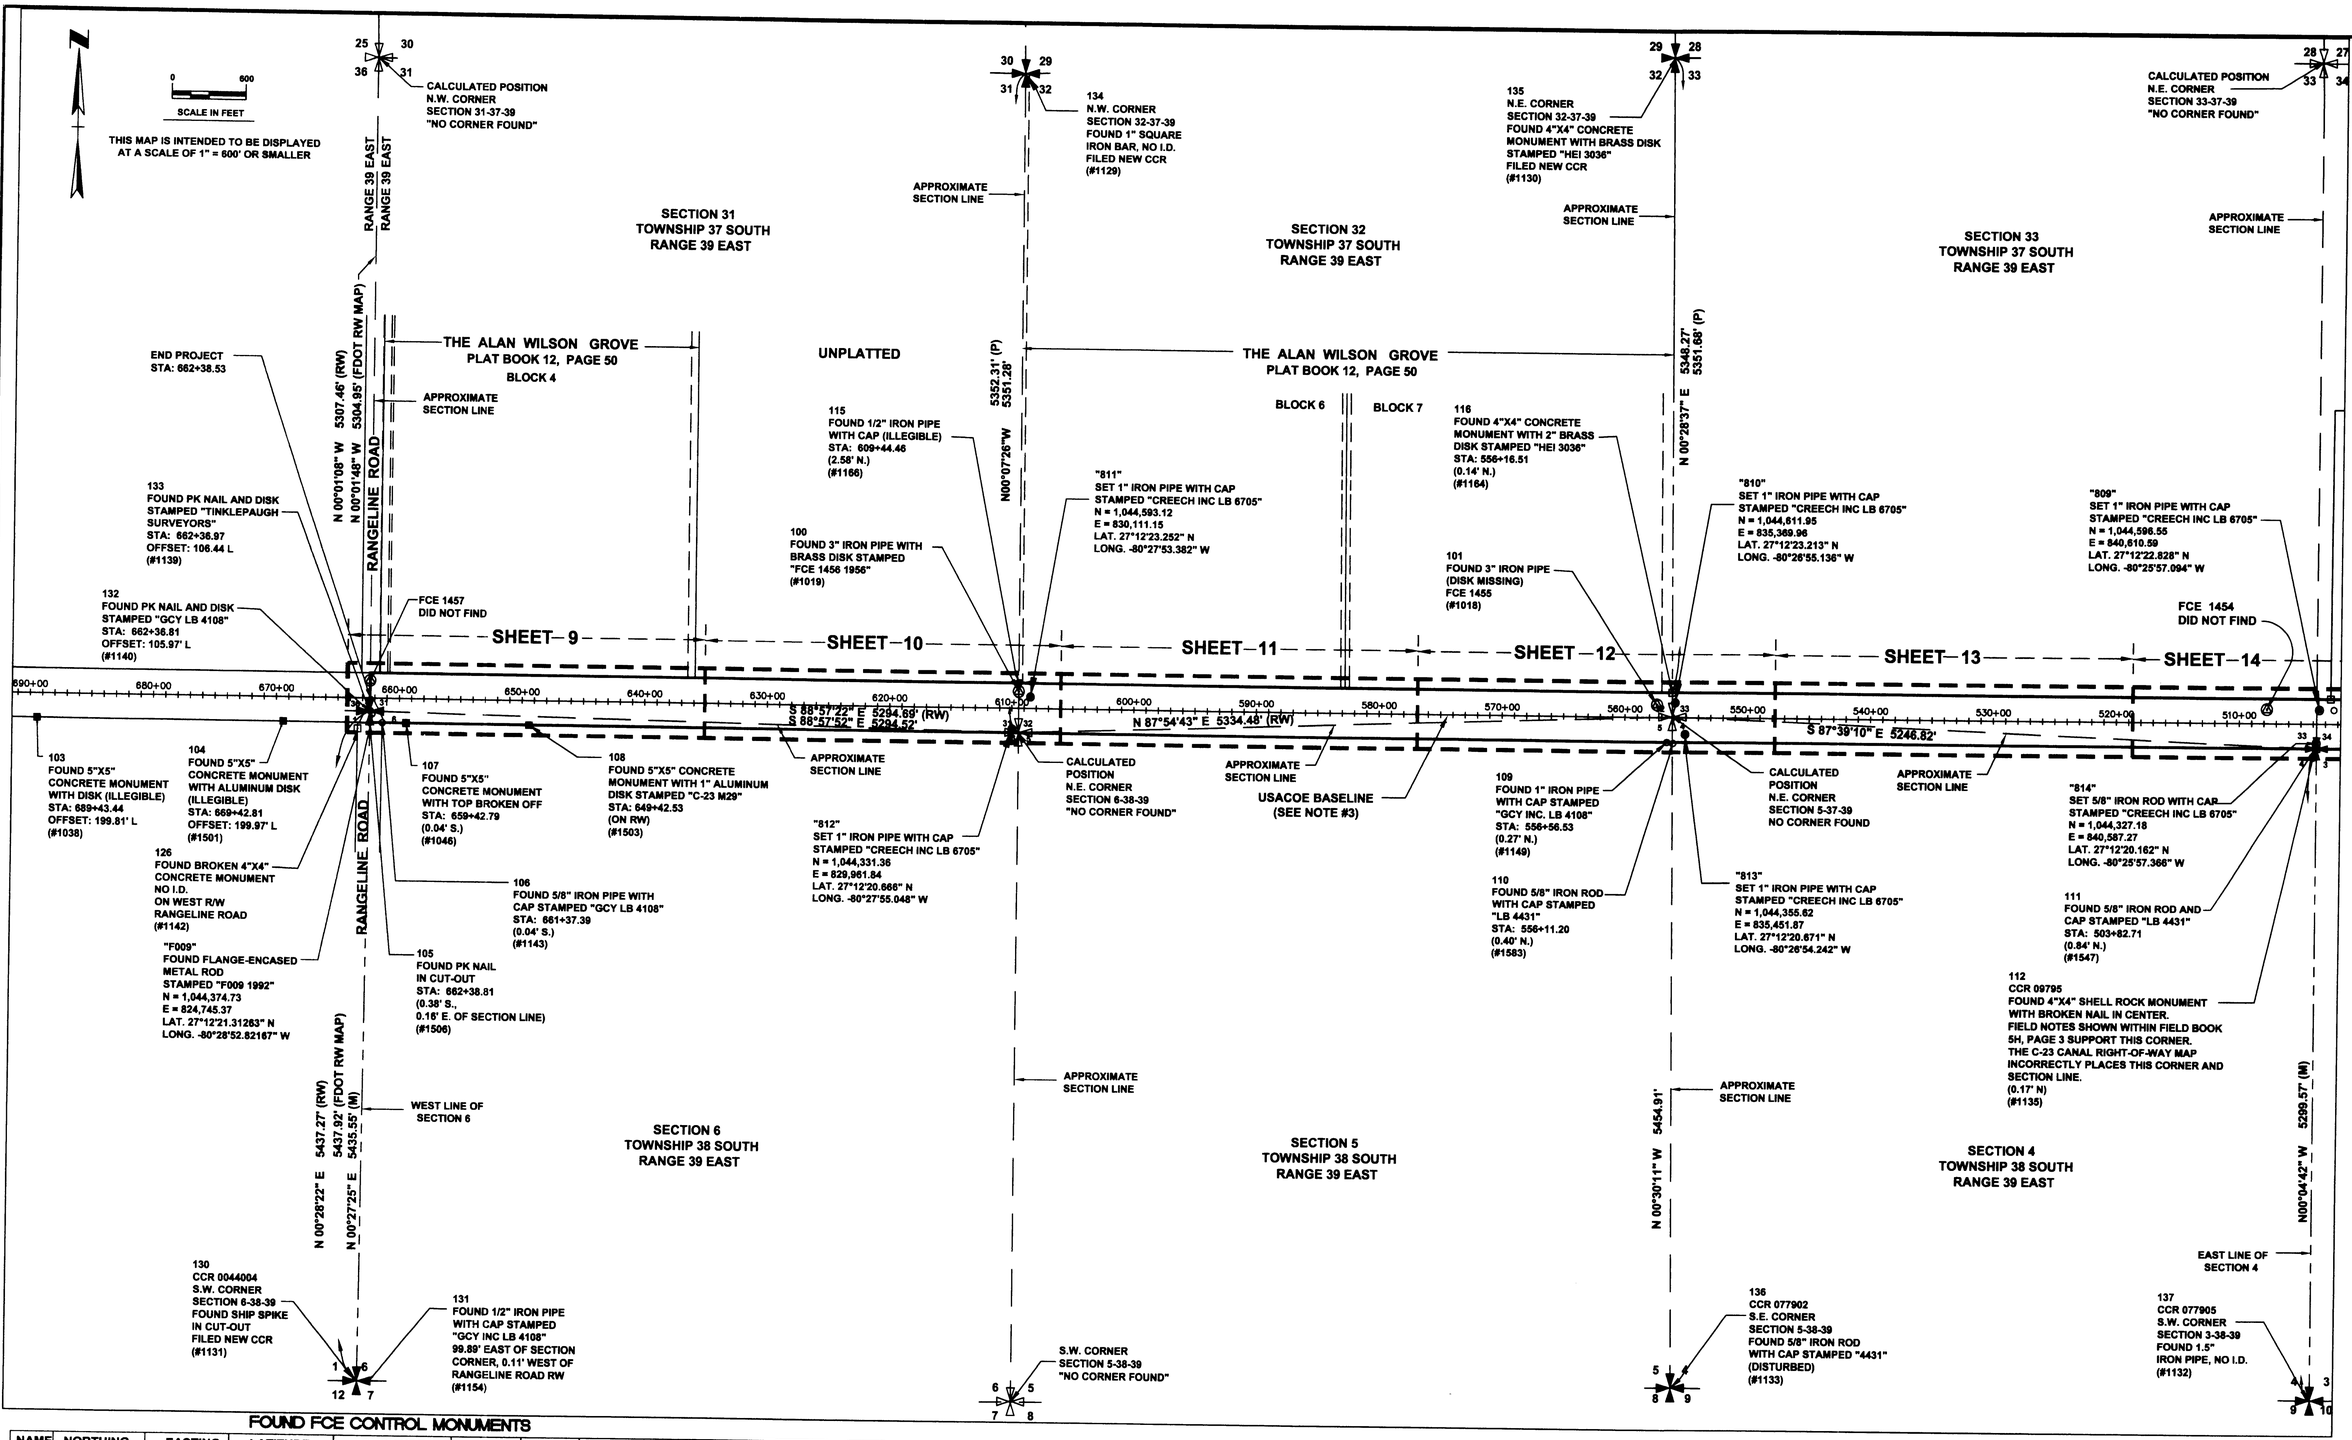

FOUND FCE CONTROL MONUMENTS

NAME	NORTHING	EASTING	LATITUDE	LONGITUDE	STATION	OFFSET	DESCRIPTION
100	1044634.35	830015.89	27° 12' 23.664" N	-80° 27' 54.435" W	609+45.06	134.44R	3" IRON PIPE WITH BRASS DISK "FCE 1456 1956"
101	1044595.03	835220.80	27° 12' 23.051" N	-80° 26' 56.789" W	557+40.10	103.56R	3" IRON PIPE - MISSING DISK (FCE 1455)
102	1044623.12	845930.02	27° 12' 22.850" N	-80° 24' 58.177" W	450+30.93	149.04R	3" IRON PIPE WITH BRASS DISK "FCE 1453 1956"

U.S.A.C.O.E. BASELINE

	NORTHING	EASTING	LATITUDE	LONGITUDE
BEGIN PROJECT STATION 334+79.38	1044461.03	856481.32	27°12' 20.744 N	-080°23' 01.325 W
N 89°56'56" W 5239.92 '				
P.I. STATION 397+19.30	1044465.70	851241.41	27°12' 21.042 N	-080°23' 59.359 W
N 89°54'35" W 5317.32'				
P.I. STATION 450+36.62	1044474.08	845924.09	27°12' 21.374 N	-080°24-58.250 W
N 89°54'25" W 21201.90'				
END PROJECT STATION P.I. STATION 662+38.53	1044508.51	824722.22	27°12' 22.638 N	-080°28-53.072 W

SET CONTROL MONUMENTS

NAME	NORTHING	EASTING	DESCRIPTION	LATITUDE	LONGITUDE
804	1,044,627.79	851,763.02	SET 1" IRON PIPE AND CAP STAMPED "TRAVERSE LB 6705"	27° 12' 22.623" N	-80° 23' 53.573" W
805	1,044,304.67	852,222.44	SET 1" IRON PIPE AND CAP STAMPED "TRAVERSE LB 6705"	27° 12' 19.401" N	-80° 23' 48.502" W
808	1,044,576.43	845,656.92	SET 1" IRON PIPE AND CAP STAMPED "CREECH INC LB 6705"	27° 12' 22.400" N	-80° 25' 01.204" W
809	1,044,596.55	840,610.59	SET 1" IRON PIPE AND CAP STAMPED "CREECH INC LB 6705"	27° 12' 22.828" N	-80° 25' 57.094" W
810	1,044,611.95	835,369.96	SET 1" IRON PIPE AND CAP STAMPED "CREECH INC LB 6705"	27° 12' 23.213" N	-80° 26' 55.136" W

SET CONTROL MONUMENTS (CONTINUED)

NAME	NORTHING	EASTING	DESCRIPTION	LATITUDE	LONGITUDE
811	1,044,593.12	830,111.15	SET 1" IRON PIPE AND CAP STAMPED "CREECH INC LB 6705"	27° 12' 23.252" N	-80° 27' 53.382" W
812	1,044,331.36	829,961.84	SET 1" IRON PIPE AND CAP STAMPED "CREECH INC LB 6705"	27° 12' 20.666" N	-80° 27' 55.048" W
813	1,044,355.62	835,451.87	SET 1" IRON PIPE AND CAP STAMPED "CREECH INC LB 6705"	27° 12' 20.671" N	-80° 26' 54.242" W
814	1,044,327.18	840,587.27	SET 5/8" IRON ROD AND CAP STAMPED "CREECH INC LB 6705"	27° 12' 20.162" N	-80° 25' 57.366" W
815	1,044,322.35	845,643.18	SET 5/8" IRON ROD AND CAP STAMPED "CREECH INC LB 6705"	27° 12' 19.884" N	-80° 25' 01.369" W

SEE SHEETS 7 AND 8 FOR FOUND MONUMENTATION TABLES

SOUTH FLORIDA WATER MANAGEMENT DISTRICT
REAL ESTATE DEPARTMENT – SURVEY SECTION
P.O. BOX 24680
3301 GUN CLUB ROAD
WEST PALM BEACH, FLORIDA 33416-4680

REVISIONS | DATE | DRAWN | CHECKED

DRAWN: DAL | CHECKED: PBM | DWG. DATE: 12-20-10 | SCALE: 1"=200'
FIELD PERSON(S): SEYMOUR-MARSHALL-CORNAM-WEDS
FIELD DATES: 1/11-13-25-26/12-2-3/2010
FIELD BOOKS: 10-86/06-97/06-96/11-90
PAGES: 1-4/5-54/55-64/65-76/7-7/8-44/7-45/1-65/
DATA COLLECTOR FILES: 26102.RWAW

PORTION OF C-23 CANAL
KEY SHEET AND PROJECT CONTROL
SECTIONS 31, 32, 33, 34, 35 AND 36, TOWNSHIP 37 SOUTH, RANGE 39 EAST
AND SECTIONS 1, 2, 3, 4, 5 AND 6, TOWNSHIP 38 SOUTH, RANGE 39 EAST

DRAWING NO. 26102.96
CAD FILE NO. 26102.96 SFWMD C23 BNDY SURVEY.dwg

6 SHEET OF 25

PLOT SCALE: 1" = 1" (PAPER SPACE)
